

A black and white photograph of a construction site. In the foreground, there are large rectangular concrete foundations for a building, with wooden forms and bracing visible. The forms have the word 'ADVANCE' printed on them. In the background, there is a large, modern building with a dark facade and large windows. To the left of the building, there is a fenced-in area with some construction equipment and materials. The sky is overcast.

Summer 2024 Construction Update

Capital Construction Projects

D214 Internal Projects

BGHS Fields Renovation: Phase 1




- Mass excavation is completed
- All tennis court and softball field posts are installed
- All tension netting poles are set
- Dugouts and concessions footings and foundation walls are poured and backfilled. Slabs will be poured this week
- Ticket booth and officials shelter lagging behind due to a gas line that needed to be re-routed (Work started on 8/20)
- Tennis court surface has begun being installed
- Field turf is set to mobilize on 8/26 for the auxiliary field



BGHS Boiler Replacement



- Boilers have been installed, started up, and have been inspected and passed by the State Fire Marshal
- Domestic Hot Water Heaters are installed and will be started this week
- The building automation system is now operating the new equipment
- Facility personnel will be given training and access to the Trane interface
- Commissioning the system will be scheduled when weather permits

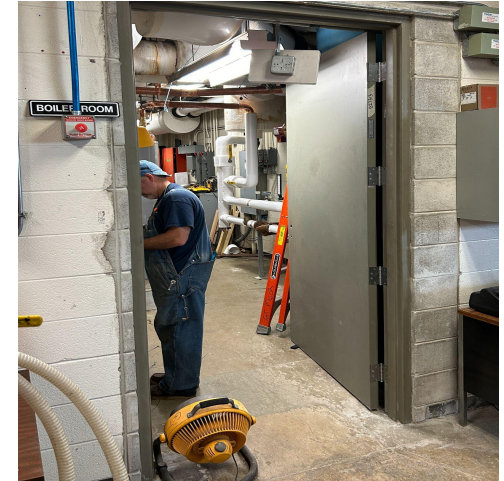

EGHS Student Services




- Updated offices for Counselors, Deans, etc.
- New nurses space
- New Attendance area
- College Career Center
- New RTU and HVAC components
- All new furniture



EGHS Culinary Arts



- Ceiling grid was completed last week
- Floor moisture mitigation
- This week quarry tile and grout will be installed
- Monday the 26th food service equipment starts being installed

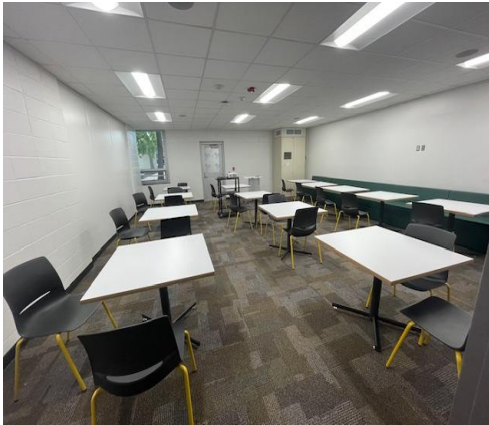

PHS Roof Replacement




- The roof was completed in time for the start of school
- All RTU units were tested and balanced
- Stair tower and all materials were removed from the building
- The punch list walk through found two minor items and they were addressed
- Commissioning of the new RTU units is still to follow



PHS Pool Repairs



- Pool repairs have been completed
- All systems were up and running on August 12th
- There will be six months of chemical monitoring and balancing from the pool contractor (As per scope of work)
- Plaster brushing will be done through this week, to make sure there is no scale build up while the plaster cures

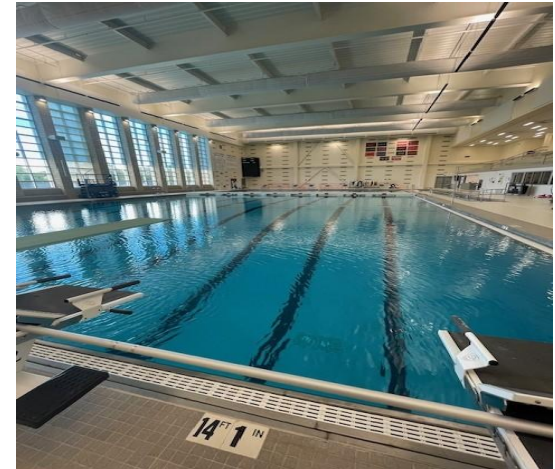

Main Gym Refinish: EGHS, JHHS, WHS



Parking Lot Painting and Striping


JHHS



RMHS



PHS

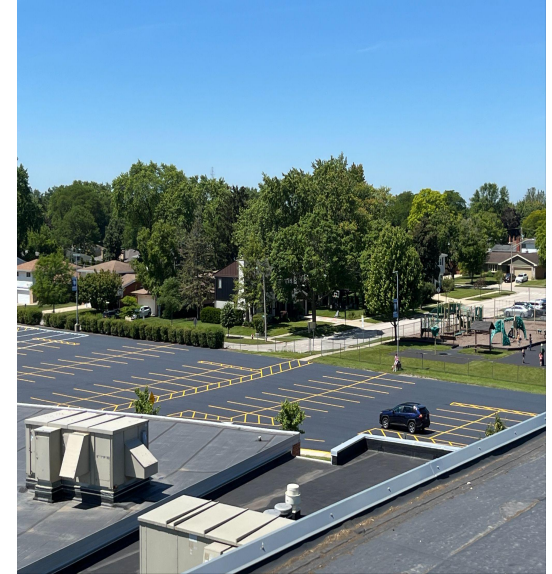

Energy Savings Projects



- One additional charging station at PHS
- LED fixture replacement by building:
 - BGHS - 264
 - EGHS - 267
 - JHHS - 122
 - PHS - 218
 - RMHS - 55
 - WHS - 50
 - **District Total - 976**



Rolling Meadows Internal Projects



- Fresh paint: 12 classrooms, student service hallway, 18 counselor offices
- Community Room: new flooring and paint
- World Language and Social Science Wing: removed eight Hauserman walls and installed new drywall with fresh paint
- 1st-floor hallway: lockers removed, new floor and paint



Wheeling Internal Projects




- Cafeteria: serving line area ceiling grid update and light replacement
- Room 103, 105, 190: fresh paint and new flooring
- 256M office painted, new floor, and lights



Prospect Internal Projects

- Special Education office: fresh paint and new lights
- ARC room new paint and flooring
- Pool lockers painted
- Courtyard and landscaping improvements
- Fitness center painted

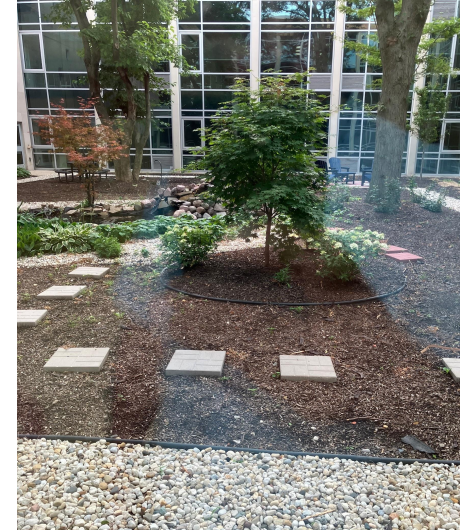

Elk Grove Internal Projects



- Fitness center painted and new lightning
- Cafeteria and foyer: new lights project cafeteria
- Main gym bleachers: new paint
- Lockers painted on a section of the second floor



Forest View Internal Projects



- Commons area light replacement and new ceiling paint
- Forest Brew: new floor, lights and paint
- Parking lot striping and curb painting
- Railing replacement around A building



Hersey Internal Projects



- Exterior doors and frames repainted
- Two bathrooms: new paint, partitions and flooring
- Carter Gym: new paint and graphics
- Exterior power washing



Buffalo Grove Internal Projects



- Main foyer and main office: LED light replacement
- Coaches Locker Room: new floor and paint

